



January 27, 2023

Aggregate Submittal
Class C
Q&D – Mustang Plant
12050 I-80 E, Sparks NV 89434

Project Name:

Q&D is pleased to provide our AASHTO accredited laboratory test results for Class C. The material was tested using the applicable test methods cited on the Submittal Document. The material meets all SSPWC specifications listed on the Submittal Document.

We trust this is the information you require at this time. If you have any questions, please do not hesitate to contact me at (775) 342-6000.

Sincerely,

A handwritten signature in blue ink, appearing to read 'N. Davis', is positioned above the typed name.

Norm Davis
Quality Control Manager

SERVICE. INTEGRITY. QUALITY.

P.O. Box 10865, Reno, Nevada 89510 | Main Office: 775.786.2677 | Fax: 775.786.5136
www.qdconstruction.com | NCL: 8197 A & B




Q&D CONSTRUCTION
est. 1964

Compliance Summary

Product Information

Plant Id 36
Plant Name Mustang Facility
Product Id 6005
Product Name 3/4" Aggregate Primary
Specification 3/4" Class C Drain Rock

Period 12/01/2022 - 01/25/2023

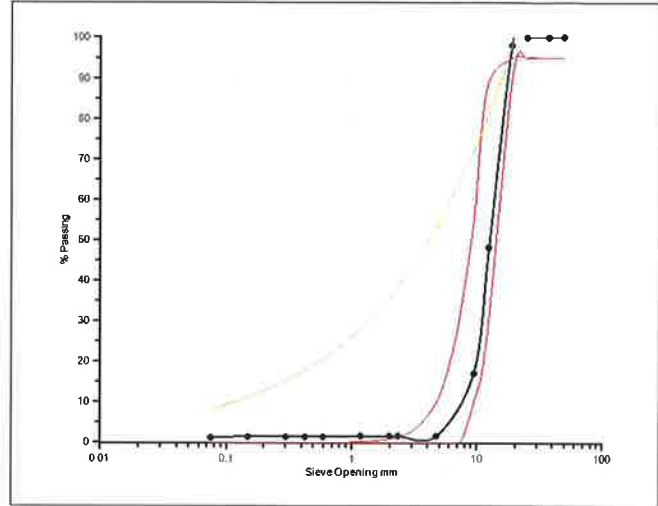

Gradation Results

Quality Results

Sieve	% Passing	Tolerances	Test	Result	Unit	Tolerances	Method
2" (50mm)	100.0		LA Abrasion (A,500)	14.2	%	≤37	ASTM C131
1 1/2" (37.5mm)	100.0		-#200 (75um)	1.29	%		AASHTO T11
1" (25mm)	100.0	100-100					
3/4" (19mm)	98.2	90-100					
1/2" (12.5mm)	48.1						
3/8" (9.5mm)	17.2	10-55					
#4 (4.75mm)	1.7	0-10					
#8 (2.36mm)	1.6						
#10 (2mm)	1.6						
#16 (1.18mm)	1.6						
#30 (.6mm)	1.5						
#40 (.425mm)	1.5						
#50 (.3mm)	1.5						
#100 (.15mm)	1.5						
#200 (75µm)	1.29						
